




# Infection center monitoring in the Troitsky and Novomoskovsk administrative districts


30/03/2020

## Layout of the monitoring object

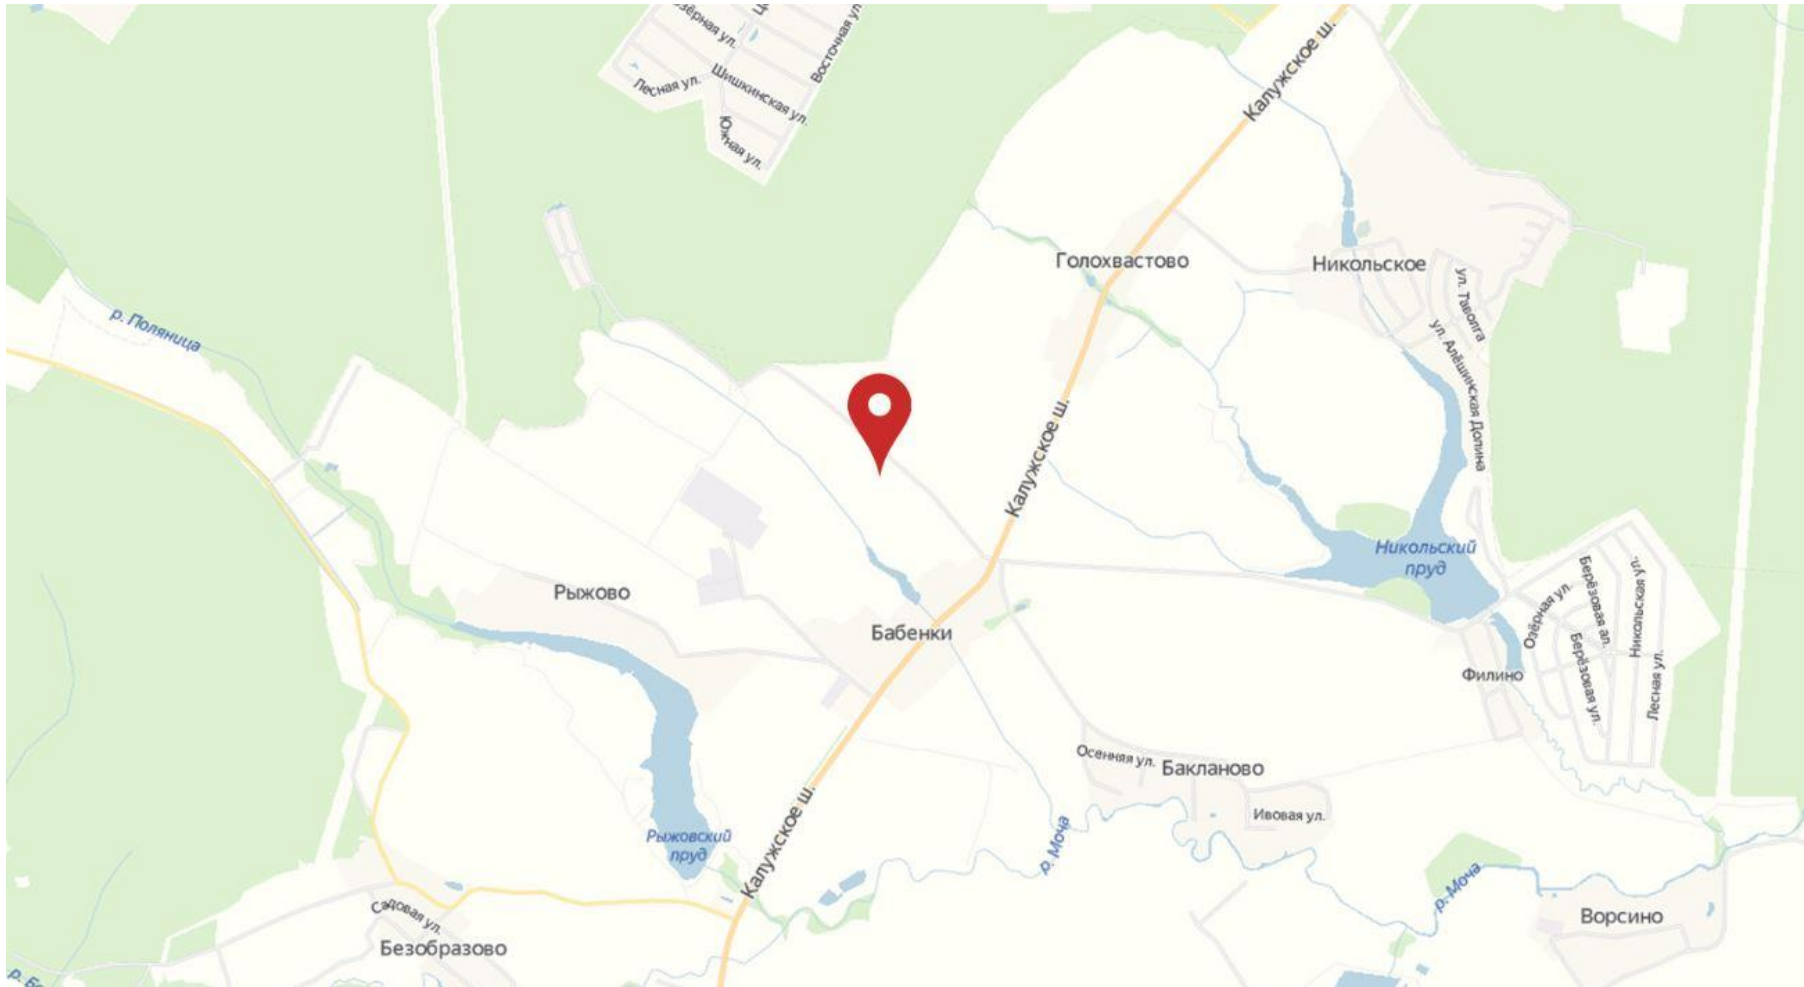

Monitoring object: Infection centre in the Troitsky and Novomoskovsky administrative areas  
Address: settlement Voronovskoe, near the village Golokhvastovo

# Infectious diseases hospital (Golokhvastovo)

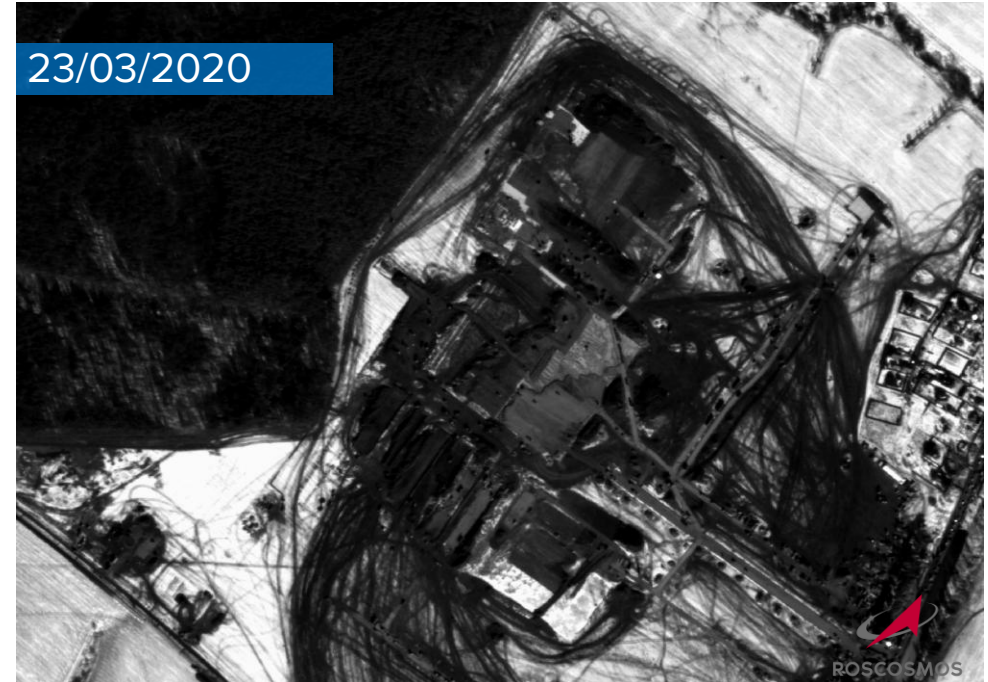

Construction began on March 12, 2020

As of March 23, 2020, preparatory work is being carried out on the construction site

- Plot fencing
- Construction of temporary infrastructure: roads, engineering networks laying
- Temporary administrative and household premises construction



# Infectious diseases hospital (Golokhvastovo)

Current state

28/03/2020



- Block A (Treatment block):
  - A1...A7 - Medical blocks
  - A8 - Pathology unit
  - A9 – the unit for the waste decontamination
  - A10 - Laboratory unit
  - A11 - Economic block
  - A12 - Washing and sanitation unit

- Block B (intensive care unit):
  - B1...B8, B10 - Intensive care units
  - B9 - Operating unit
  - B9a - Diagnostic unit
  - B11 - Receiving unit
  - B12 - Healthy patient discharge block
  - B13 - Laundry and storage room for personal belongings
  - B14 - Equipment sterilization center
  - B15 – Sanitary Inspection
  - B16 - Vehicle washing unit

- Block C (Service block):
  - B1...B12, B18 - Dormitories blocks
  - B13 - Administration block
  - B14, B17 - Warehouse inventory
  - B15 - Medicine warehouse
  - B16 - Food unit
  - B19 - Control room

# Block A (Treatment block)

## Current state



Block A:

Medical blocks A1...A4 - 75% of the building frame has been constructed.

Medical blocks A5...A7 - work on the construction of the frame of the building was completed by 65%.

Block A8 (Pathoanatomic block) - 85% of the roofing work has been completed.

Block A9 (waste decontamination Unit) - roof works are completed by 50%.

Block A10 (Laboratory block) - installed the frame of the building, roofing works has started.

Block A11, A 12 - Frame of the 1st floor construction is underway.



# Block B (intensive care Unit)

## Current state



Block B:

Block B 1 - construction of the building frame is finished by 25%.

Block B2 - installation of the reinforced foundation is 90% complete.

Block B3, B4, B8 - roofing works are 100% completed.

Block B5 - installation of reinforced foundation is 85% complete.

Block B6, B7 - roofing works are completed by 70%.

Block B9 - work has not started yet.

Block B10 - reinforced concrete works are underway to install foundation blocks.

Block B11 (Receiving block) - concrete work on the foundation is underway.

Block B12, B13, B14, B15, B16 - construction of the roof has started.



# Block C (Service block)

## Current state



Block C:

Block C1...C12, C18 (Service blocks) - concrete works are underway: construction and waterproofing of the foundation.

Block C13 (administration block) - roofing works are 100% completed.

Blocks C14, C17 (inventory warehouse) - roofing works are completed by 85%.

Block C15 (storage of medicines) – roofing works are completed.

Block C16 (food hall) - roof work completed.

# Number of working construction equipment

